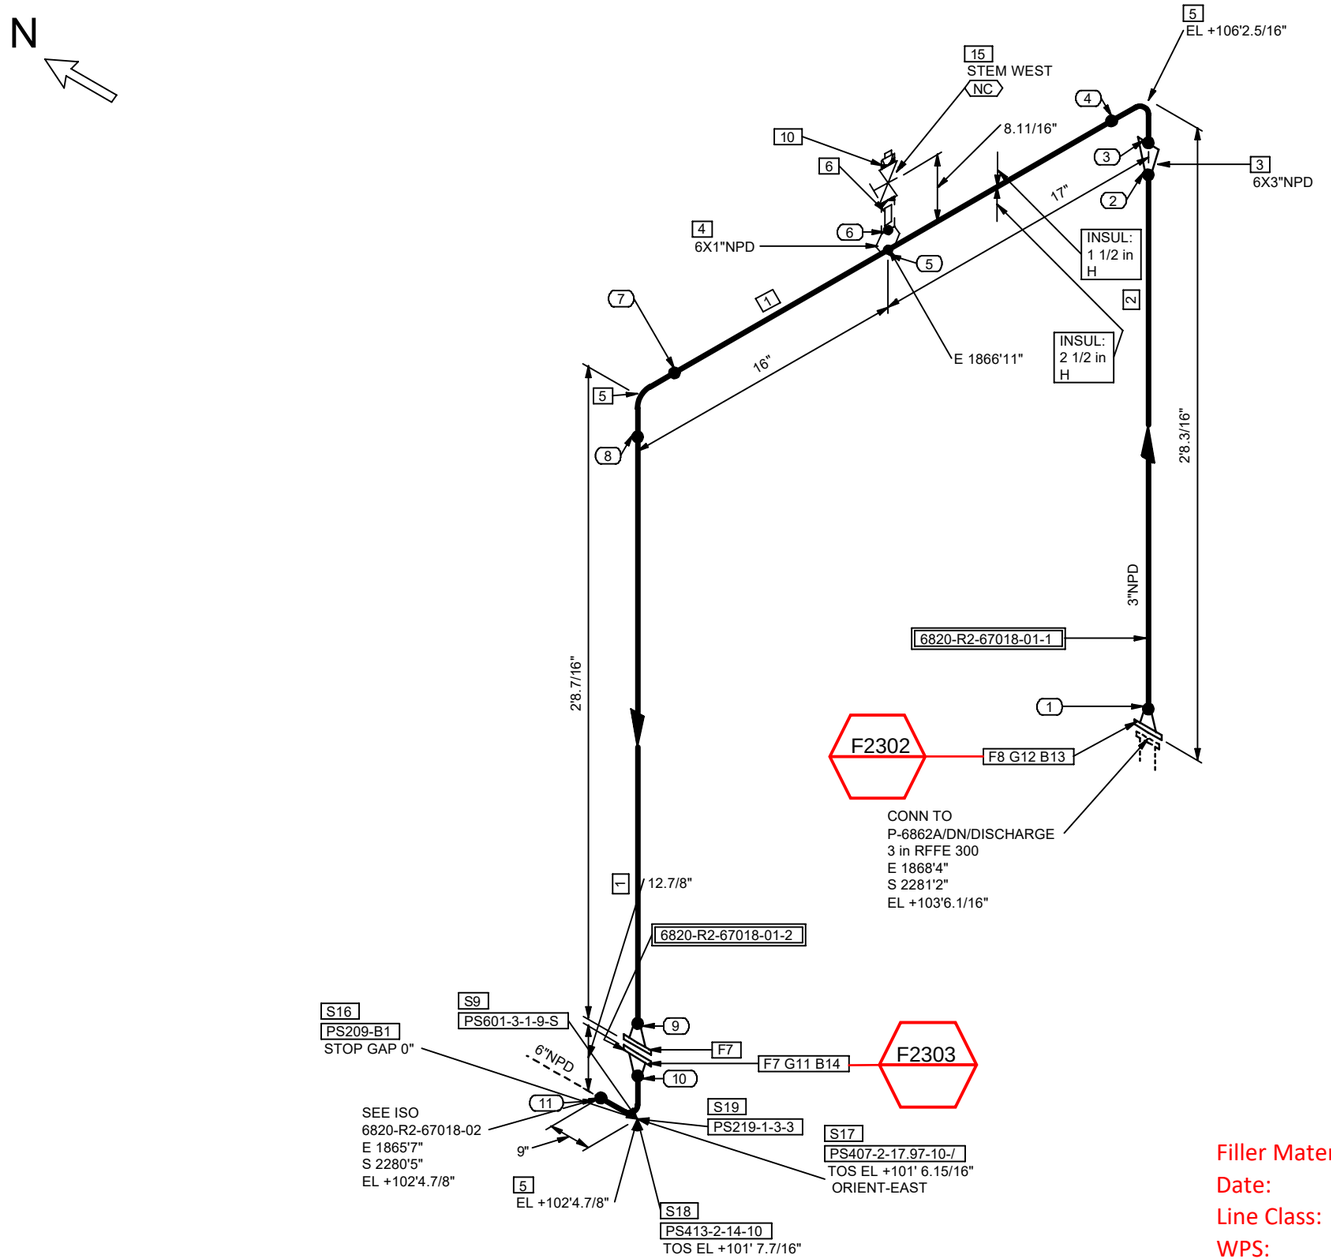

COORDINATE SYSTEM : PLANTCOORDINATES

Filler Material Requisition

Date: 8-14-24

Line Class: SCXL-CS02

WPS: 10245

Electrode: ER70S-2

Signature: Pedro Morin

SHOP MATERIALS

NO	NPD	DESCRIPTION	IDENT	QTY
1	6	Pipes, Seamless, ASME B36.10, ASTM A106 Gr.B, BE, -, -, S-STD	CPP00336	2.9 '
2	3	Pipes, Seamless, ASME B36.10, ASTM A106 Gr.B, BE, -, -, S-STD	CPP002ZK	1.3 '
3	6X3	Conc Reducer, Seamless, ASME B16.9, ASTM A234 Gr.WPB, BW Ends, -,-, S-STD	CDB68SYR	1
4	6X1	Sockolet, ASTM A105N, 3000 Lbs, SW Ends, -, -,	CYU3EY	1
5	6	90° Elb LR, Seamless, ASME B16.9, ASTM A234 Gr.WPB, BW Ends, -,-, S-STD	CDB66GNP	3
6	1	Nipple, ASTM A106 Gr.B, PE/NPTM End, L = 3in, -, S-XS	C12GGPTC	1
7	6	WN Flg, ASME B16.5, ASTM A105N, 300 Lbs, RF/BW End, -, S-STD	CFG6WKU7	2
8	3	WN Flg, ASME B16.5, ASTM A105N, 300 Lbs, RF/BW End, -, S-STD	CFG6WKPL	1

PIPE SUPPORTS

9	6	PS601-3-1-9-S	PS601	1

OTHER THAN SHOP MATERIALS

NO	NPD	DESCRIPTION	IDENT	QTY
10	1	Plug, Solid Round Head Type, ASME B16.11, ASTM A105N, NPTM End, -,	CBBPLK4	1
11	6	NM Flat Gk, Barium Sulfate filled PTFE, 300 Lbs, RF as per ASME B16.5, Full Face, Thk=1/8in, -,	C7CX7CST	1
12	3	NM Flat Gk, Barium Sulfate filled PTFE, 300 Lbs, RF as per ASME B16.5, Full Face, Thk=1/8in, -,	C7CX7CSN	1
13	3/4	SBlt 2 HHx N, A193 Gr.B7/A194 Gr.2H, -, Xylan PTFE Coated, -4.25 in. Length	C6S4K8BC	8
14	3/4	SBlt 2 HHx N, A193 Gr.B7/A194 Gr.2H, -, Xylan PTFE Coated, -5 in. Length	C6S4K8BF	12
15	1	Gat Fem, API 602, ASTM A105N,800 Lbs, NPTF Ends, HO,-, Valve Tag: GA-0120	C76SPABV	1

PIPE SUPPORTS

16	6	PS209-B1	PS209	1
17	6	PS407-2-17.97-10-/	PS407	1
18	6	PS413-2-14-10	PS413	1
19	6	PS219-1-3-3	PS219	1

PIECE MARKS

6820-R2-67018-01-1 6820-R2-67018-01-2

Turner Industries Group, LLC
Received
August 12,2024
DOCUMENT CONTROL

NOTES:

1. FOR LINE PRESSURES, TEMPERATURES, INSULATION TYPE AND THICKNESS, ETC. REFER TO LATEST REVISION OF LDT.
2. FOR STANDARD PIPE SUPPORT DETAILS SEE PROJECT STANDARD.
3. FIELD SHIM TO SUIT UNLESS OTHERWISE NOTED.
4. FOR PWHT REQUIREMENTS REFER TO LINE CLASS SPECIFICATION.
5. ALL THREADED PIPE LINE SYSTEMS, FIELD SHALL VERIFY DIMENSION PRIOR TO ERECTION.
6. FFW DESIGNATION AT WELDS INDICATES FIELD FIT WELD, WHERE PIPE FABRICATOR IS TO ADD 9 INCH OF PIPE TO THE ISOMETRIC DIMENSION TO ENABLE THE FIELD TO CUT TO FIT AT SITE.
7. REFER TO 202998C-000-W1-1300-0001 FOR FRP AND DUAL-LAM FABRICATION.

TECHNIP ENERGIES

information contained in this document is the work product of one or more legal entities of Technip Energies N.V. and embodies confidential and proprietary information of the applicable entity and/or its client.use of this information is restricted in accordance with conditions specified by the contract.Technip Energies N.V. and its affiliates disclaim any and all liabilities for any changes or modifications to this document which are made by any person other than the entity that issued the document under the applicable client contract.

THIS DOCUMENT IS UNCONTROLLED WHEN REPRODUCED

REV	DATE	BY	DESCRIPTION	CHKD	MTO	STRESS	APRVD
0	2024-08-09	RVA	ISSUED FOR CONSTRUCTION	SAD	KJK	SMR	GR

SERVICE:	VAPOR/LIQUID:	INSUL TYPE:	INSUL THK:	SHOP:	FIELD:	PAINT CODE:	MODULE:
R2	L	Per LDT	Per LDT	Y	Y	Per LDT	-

OXY

OxyChem Redstone Battleground PROJECT

P&ID: 202998C-001-PID-0021-0321

UNIT#:	EWP AREA:	SPEC:	STRESS CALC #:
6800	6820	SCXL-CS02	CN-0385

LINE No. 6"-R2-67018-SCXL-CS02-H

DRAWING NUMBER: 6820-R2-67018-01

REV.: 0

09 AUG 2024 08:04
