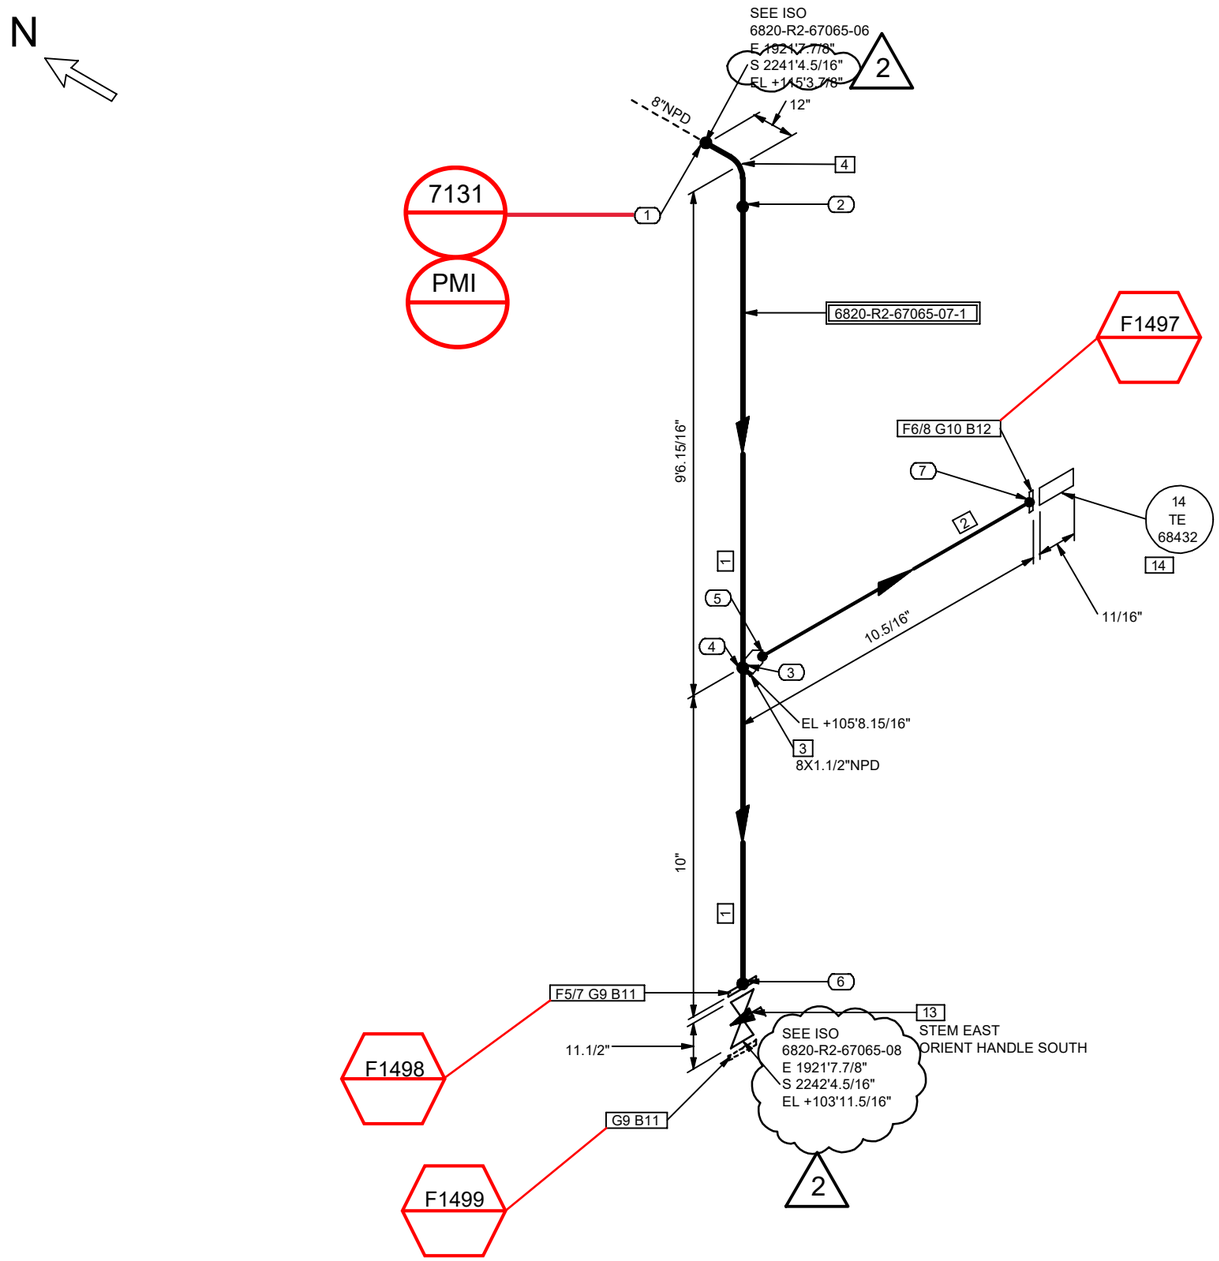

COORDINATE SYSTEM : PLANTCOORDINATES

Filler Material Requisition

Date: 1-31-25

Line Class: NOHD-NI01

WPS: 4130

Electrode: ERNi-1

Signature: Glenn Sumrall Jr

SHOP MATERIALS

NO	NPD	DESCRIPTION	IDENT	QTY
1	8	Pipes, EFW, ASME B36.19/B36.10, ASTM B725 UNS N02200 annealed, BE, -, -, S-10S	C7ZWWML7	9.1 '
2	1.1/2	Pipes, Seamless, ASME B36.19/B36.10, ASTM B161 UNS N02200, BE, -, -, S-10S	C7ZWWMRJ	0.3 '
3	8X1.1/2	Weldolet, MSS SP-97, ASTM B366 Gr.WPN, BW Ends, Annealed, S-10S	C7ZX02VA	1
4	8	90° Elb LR, Seamless, ASME B16.9, ASTM B366 Gr.WPN, BW Ends, -,Annealed, S-10S	C7ZWX04P	1
5	8	LJ Flg, ASME B16.5, ASTM A105 Galv. as per ASTM A153, 150 Lbs, FF, -,	C26WFFFR	1
6	1.1/2	LJ Flg, ASME B16.5, ASTM A105 Galv. as per ASTM A153, 150 Lbs, FF, -,	C26WFFF9	1

MISCELLANEOUS COMPONENTS

7	8	Stub SP, Seamless, ASME B16.9, ASTM B366 Gr.WPN, BW Ends, -,Annealed, x S-10S	C8A5GY48	1
8	1.1/2	Stub SP, Seamless, ASME B16.9, ASTM B366 Gr.WPN, BW Ends, -,Annealed, x S-10S	C8A5GXPV	1

OTHER THAN SHOP MATERIALS

NO	NPD	DESCRIPTION	IDENT	QTY
9	8	NM Flat Gk, Barium Sulfate filled PTFE, 150 Lbs, RF as per ASME B16.5, -, Thk=1/8in, -,	C6SBWZF4	2
10	1.1/2	NM Flat Gk, Barium Sulfate filled PTFE, 150 Lbs, RF as per ASME B16.5, -, Thk=1/8in, -,	C6S4K87H	1
11	3/4	SBlt 2 HHx N, A193 Gr.B7/A194 Gr.2H, -, Xylan PTFE Coated, - 4.75 in. Length	C6S4K8BE	16
12	1/2	SBlt 2 HHx N, A193 Gr.B7/A194 Gr.2H, -, Xylan PTFE Coated, - 2.75 in. Length	C6S4K87U	4
13	8	Plug Flg,SP, Inverted Tapered Plug, Non Lubricated, API 599, ASTM A494 Gr.CZ100, 150 Lbs, RF, Ends as per ASME B16.5, -, GO,-, -, Valve Tag: PL-0503	C8P7NJK0	1

INSTRUMENTS

14	1.1/2	14-TE-68432	14-TE-68432	1

PIECE MARKS

6820-R2-67065-07-1

Turner Industries Group, LLC
Received
January 30,2025
DOCUMENT CONTROL

NOTES:

1. FOR LINE PRESSURES, TEMPERATURES, INSULATION TYPE AND THICKNESS, ETC. REFER TO LATEST REVISION OF LDT.
2. FOR STANDARD PIPE SUPPORT DETAILS SEE PROJECT STANDARD.
3. FIELD SHIM TO SUIT UNLESS OTHERWISE NOTED.
4. FOR PWHT REQUIREMENTS REFER TO LINE CLASS SPECIFICATION.
5. ALL THREADED PIPE LINE SYSTEMS, FIELD SHALL VERIFY DIMENSION PRIOR TO ERECTION.
6. FFW DESIGNATION AT WELDS INDICATES FIELD FIT WELD, WHERE PIPE FABRICATOR IS TO ADD 9 INCH OF PIPE TO THE ISOMETRIC DIMENSION TO ENABLE THE FIELD TO CUT TO FIT AT SITE.
7. REFER TO 202998C-000-W1-1300-0001 FOR FRP AND DUAL-LAM FABRICATION.

T.EN TECHNIP ENERGIES

information contained in this document is the work product of one or more legal entities of Technip Energies N.V. and embodies confidential and proprietary information of the applicable entity and/or its client.use of this information is restricted in accordance with conditions specified by the contract.Technip Energies N.V. and its affiliates disclaim any and all liabilities for any changes or modifications to this document which are made by any person other than the entity that issued the document under the applicable client contract.

THIS DOCUMENT IS UNCONTROLLED WHEN REPRODUCED

REV	DATE	BY	DESCRIPTION	CHKD	MTO	STRESS	APRVD
2	2025-01-24	RVA	ISSUED FOR CONSTRUCTION	SAD	KJK	SMR	GR
1	2024-12-10	RVA	ISSUED FOR CONSTRUCTION	SAD	KJK	SMR	GR
0	2024-08-02	RVA	ISSUED FOR CONSTRUCTION	SAD	KJK	BRD	GR

SERVICE:	VAPOR/LIQUID:	INSUL TYPE:	INSUL THK:	SHOP:	FIELD:	PAINT CODE:	MODULE:
R2	L	Per LDT	Per LDT	Y	Y	Per LDT	-

OxyChem Redstone Battleground
PROJECT

P&ID: 202998C-001-PID-0021-0325

UNIT#:	EWP AREA:	SPEC:	STRESS CALC #:
6800	6820	NOHD-NI01	CN-0393

LINE No. 8"-R2-67065-NOHD-NI01-H

DRAWING NUMBER: 6820-R2-67065-07

REV. 2

23 JAN 2025 04:38
