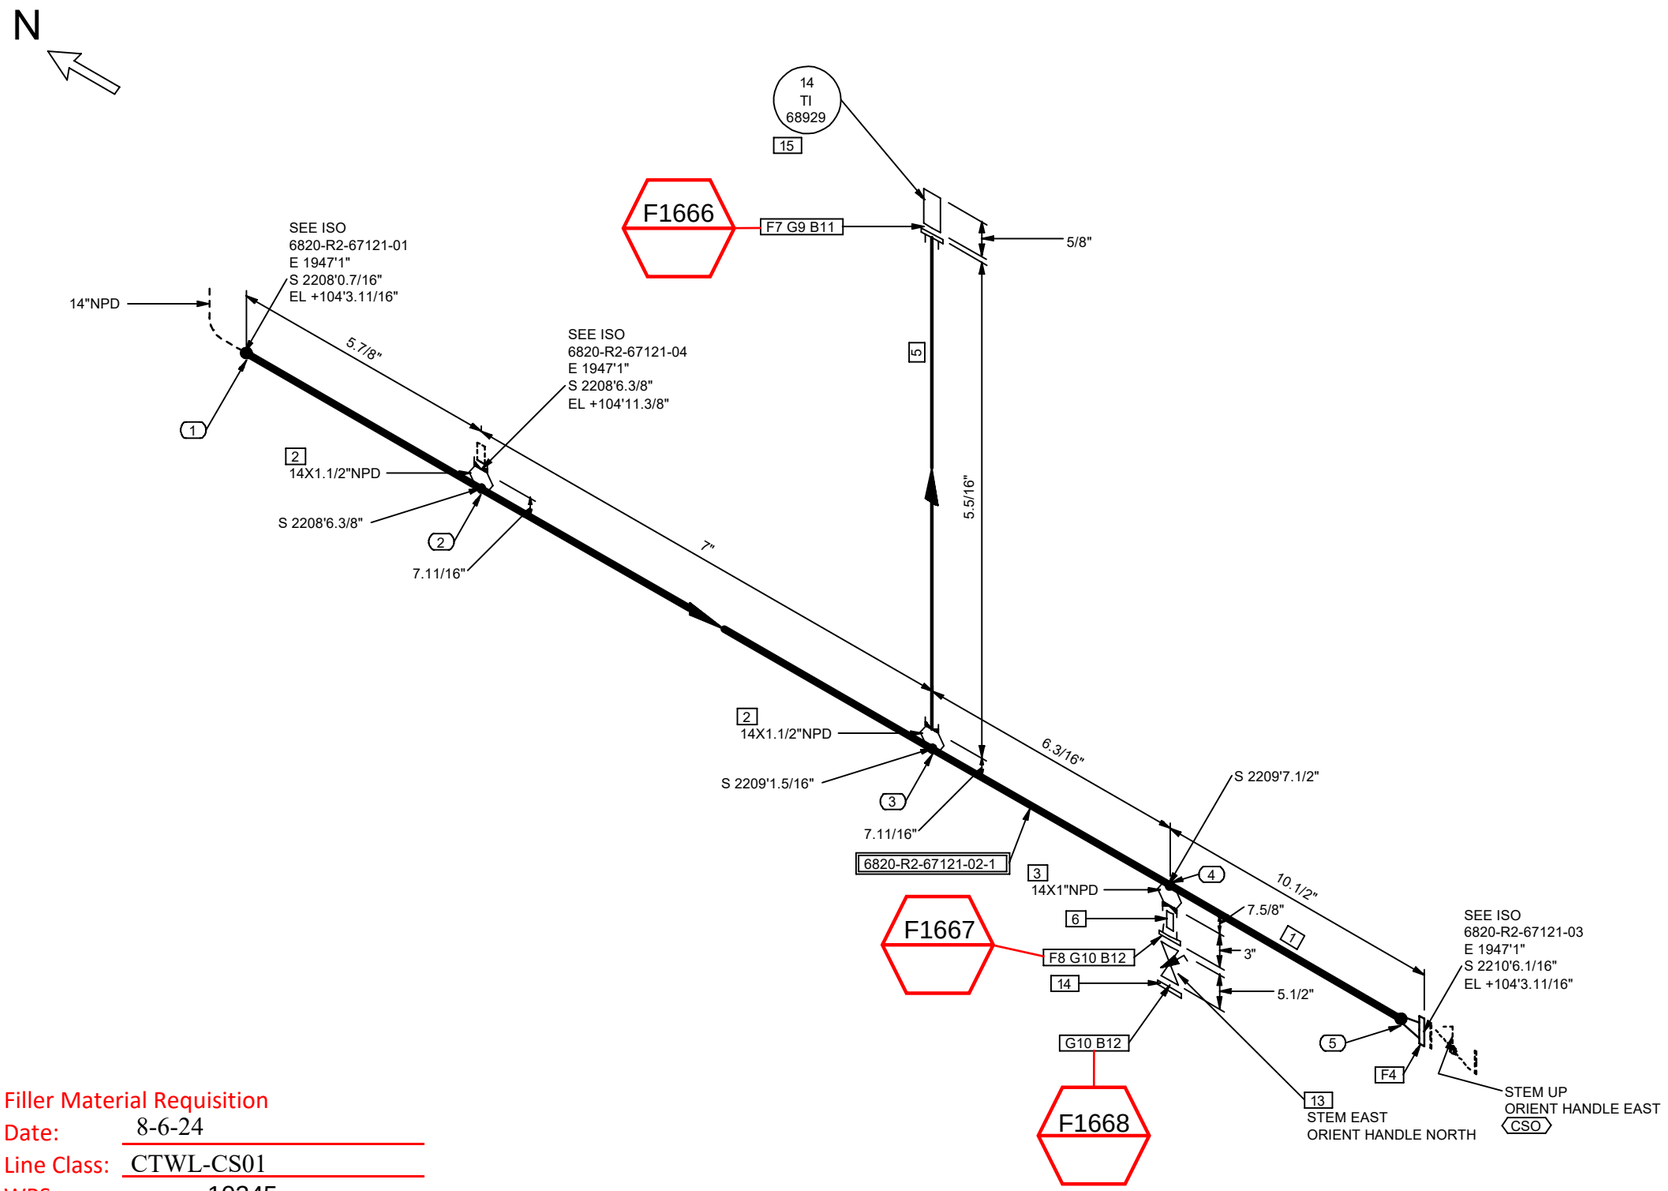

Filler Material Requisition

Date: 8-6-24

Line Class: CTWL-CS01

WPS: 10245

Electrode: ER70S-2

Signature: Pedro Morin

COORDINATE SYSTEM : PLANTCOORDINATES

SHOP MATERIALS

NO	NPD	DESCRIPTION	IDENT	QTY
1	14	Pipes, Seamless, ASME B36.10, ASTM A106 Gr.B, BE, -, -, S-STD	CPP0AMRT	2.1 '
2	14X1.1/2	Threadolet, ASTM A105N Galv. as per ASTM A153, 3000 Lbs, NPTF Ends, -, -,	C1Y177MR	2
3	14X1	Threadolet, ASTM A105N Galv. as per ASTM A153, 3000 Lbs, NPTF Ends, -, -,	C1Y177MN	1
4	14	WN Flg, ASME B16.5, ASTM A105N, 150 Lbs, RF/BW End, -, S-STD	CFG6WJ59	1

OTHER THAN SHOP MATERIALS

NO	NPD	DESCRIPTION	IDENT	QTY
5	1.1/2	Pipes, Seamless, ASME B36.10, ASTM A106 Gr.B Galv. as per ASTM A153, NPTM Ends, w/ coupling, -, S-XS	CPPD3S3F	0.5 '
6	1	Nipple, ASTM A106 Gr.B Galv. as per ASTM A153, NPTM Ends, L = 3in, -, S-XS	C41B2D94	1
7	1.1/2	THD Flg, ASME B16.5, ASTM A105N Galv. as per ASTM A153, 150 Lbs, RF/NPTF End, -,	C1DR2JP	1
8	1	THD Flg, ASME B16.5, ASTM A105N Galv. as per ASTM A153, 150 Lbs, RF/NPTF End, -,	C1DR2JM	1
9	1.1/2	NM Flat Gk, Aramid Fiber Reinforced SBR, 150 Lbs, RF as per ASME B16.5, Full Face, Thk=1/8in, -,	C76KHSS1	1
10	1	NM Flat Gk, Aramid Fiber Reinforced SBR, 150 Lbs, RF as per ASME B16.5, Full Face, Thk=1/8in, -,	C76KHSRZ	2
11	1/2	SBlt 2 HHx N, A193 Gr.B7/A194 Gr.2H, -, Xylan PTFE Coated, - 3 in. Length	C6S4K87V	4
12	1/2	SBlt 2 HHx N, A193 Gr.B7/A194 Gr.2H, -, Xylan PTFE Coated, - 2.75 in. Length	C6S4K87U	8
13	1	Plug Flg,SP, Inverted Tapered Plug, Non Lubricated, API 599, ASTM A395 Gr.60-40-18, 150 Lbs, RF, Ends as per ASME B16.5, -, LO,-, -, Valve Tag: PL-0546	C76RJXHV	1
14	1	Bld Flg, ASME B16.5, ASTM A105N Galv. as per ASTM A153, 150 Lbs, RF, -,	C1DR2JV	1

INSTRUMENTS

15	1.1/2	14-TI-68929	14-TI-68929	1

PIECE MARKS

6820-R2-67121-02-1

Turner Industries Group, LLC
Received
August 6,2024
DOCUMENT CONTROL

NOTES:

1. FOR LINE PRESSURES, TEMPERATURES, INSULATION TYPE AND THICKNESS, ETC. REFER TO LATEST REVISION OF LDT.
2. FOR STANDARD PIPE SUPPORT DETAILS SEE PROJECT STANDARD.
3. FIELD SHIM TO SUIT UNLESS OTHERWISE NOTED.
4. FOR PWHT REQUIREMENTS REFER TO LINE CLASS SPECIFICATION.
5. ALL THREADED PIPE LINE SYSTEMS, FIELD SHALL VERIFY DIMENSION PRIOR TO ERECTION.
6. FFW DESIGNATION AT WELDS INDICATES FIELD FIT WELD, WHERE PIPE FABRICATOR IS TO ADD 9 INCH OF PIPE TO THE ISOMETRIC DIMENSION TO ENABLE THE FIELD TO CUT TO FIT AT SITE.
7. REFER TO 202998C-000-W1-1300-0001 FOR FRP AND DUAL-LAM FABRICATION.

T.EN TECHNIP ENERGIES

Information contained in this document is the work product of one or more legal entities of Technip Energies N.V. and embodies confidential and proprietary information of the applicable entity and/or its client.use of this information is restricted in accordance with conditions specified by the contract.Technip Energies N.V. and its affiliates disclaim any and all liabilities for any changes or modifications to this document which are made by any person other than the entity that issued the document under the applicable client contract.

THIS DOCUMENT IS UNCONTROLLED WHEN REPRODUCED

REV	DATE	BY	DESCRIPTION	CHKD	MTO	STRESS	APRVD
0	2024-08-02	RVA	ISSUED FOR CONSTRUCTION	SAD	KJK	BRD	GR

SERVICE:	VAPOR/LIQUID:	INSUL TYPE:	INSUL THK:	SHOP:	FIELD:	PAINT CODE:	MODULE:
R2	L	Per LDT	Per LDT	Y	Y	Per LDT	-

OXY

OxyChem Redstone Battleground
PROJECT

P&ID: 202998C-001-PID-0021-0328

UNIT#:	EWP AREA:	SPEC:	STRESS CALC #:
6800	6820	CTWL-CS01	CN-0402

LINE No. 14"-R2-67121-CTWL-CS01-N

DRAWING NUMBER 6820-R2-67121-02 | REV. 0

02 AUG 2024 08:15
