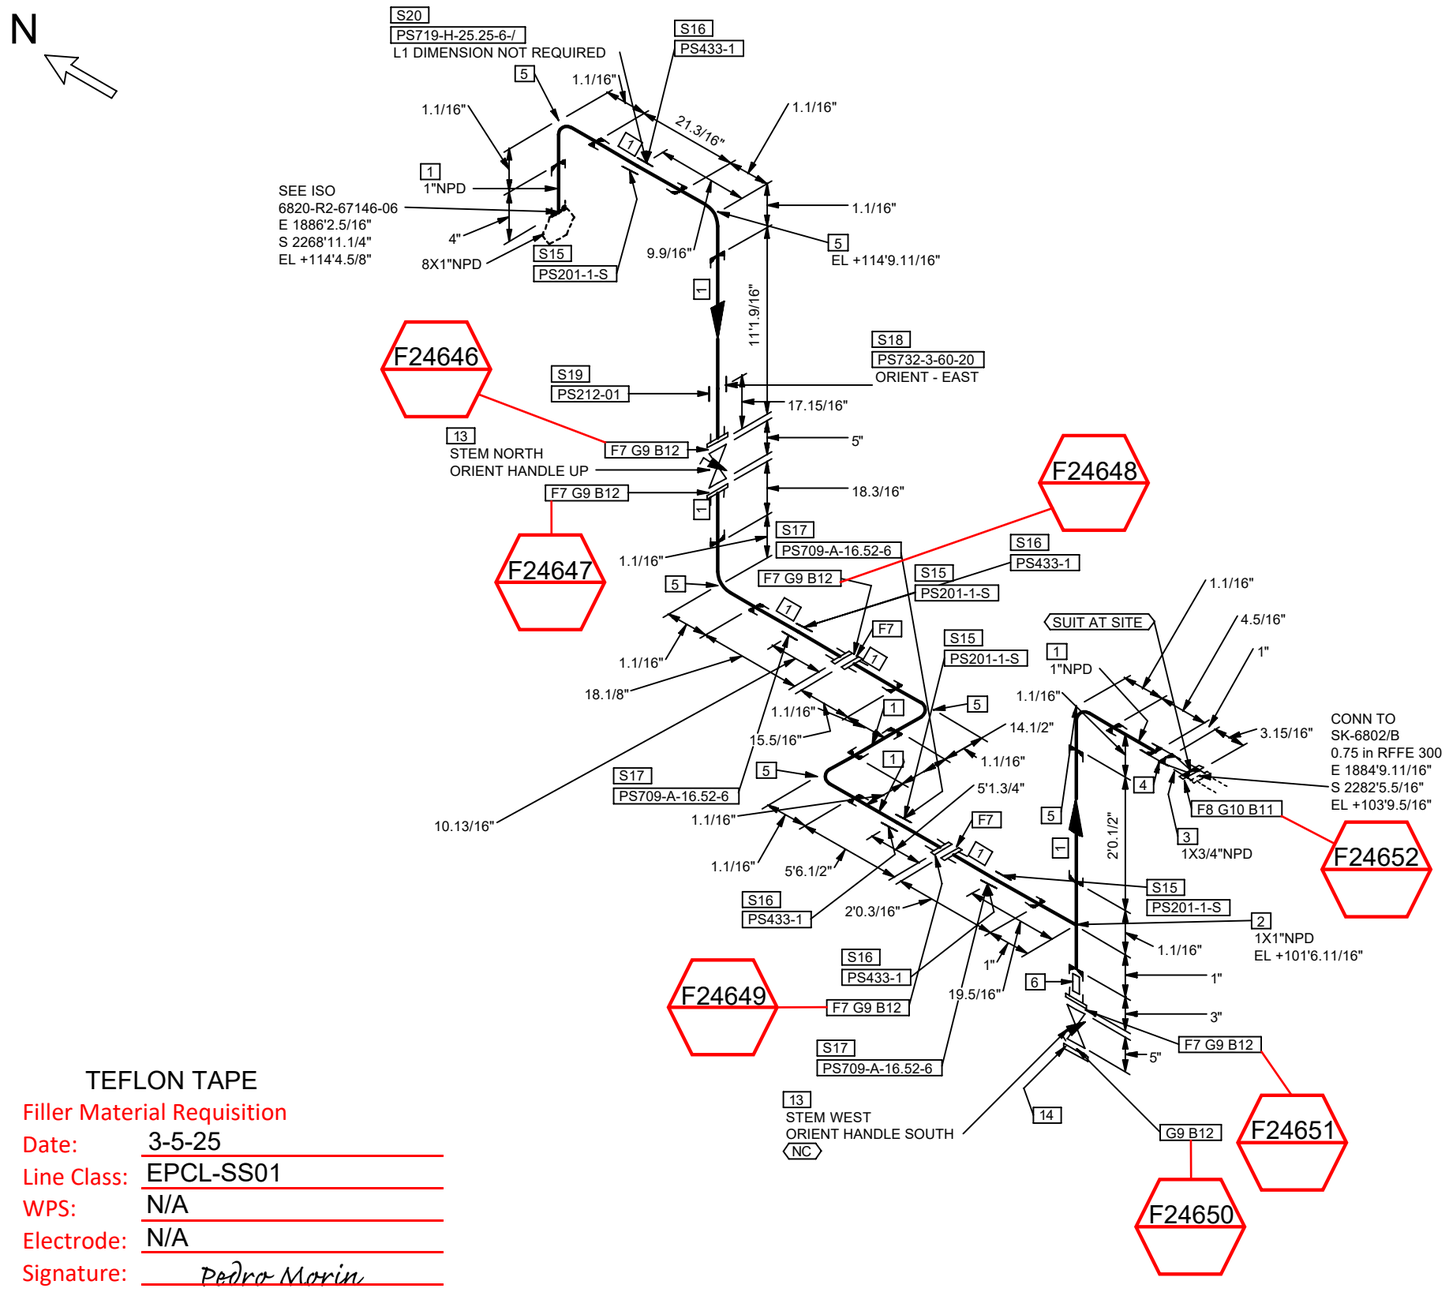

TEFLON TAPE

Filler Material Requisition

Date: 3-5-25

Line Class: EPCL-SS01

WPS: N/A

Electrode: N/A

Signature: Pedro Morin

COORDINATE SYSTEM : PLANTCOORDINATES

OTHER THAN SHOP MATERIALS

NO	NPD	DESCRIPTION	IDENT	QTY
1	1	Pipes, Seamless, ASME B36.19/B36.10, ASTM A312 Gr.TP304L, NPTM Ends, w/ coupling, -, S-80S	C76KFFTD	28.7 '
2	1X1	Eq Te, ASME B16.11, ASTM A182 Gr.F304L, 3000 Lbs, NPTF Ends, Annealed,	C7BP525C	1
3	1X3/4	Concentric swage, MSS SP-95, ASTM A403 Gr.WP304L,NPTM Ends,-, Annealed, S-80S	C7BP5XKV	1
4	1	Full Coup, ASME B16.11, ASTM A182 Gr.F304L, 3000 Lbs, NPTF Ends, Annealed,	C7BP51NV	1
5	1	90° Elb, ASME B16.11, ASTM A182 Gr.F304L, 3000 Lbs, NPTF Ends, Annealed,	C7BP5GGW	6
6	1	Nipple, ASTM A312 Gr.TP304L, NPTM Ends, L = 3in, -, S-80S	CEZMKL0	1
7	1	THD Flg, ASME B16.5, ASTM A182 Gr.F304L, 150 Lbs, RF/NPTF End, Annealed,	C7W2U48L	7
8	3/4	THD Flg, ASME B16.5, ASTM A182 Gr.F304L, 300 Lbs, RF/NPTF End, Annealed,	C7W2U48S	1
9	1	NM Flat Gk, Barium Sulfate filled PTFE, 150 Lbs, RF as per ASME B16.5, Full Face, Thk=1/8in, -,	C7CT1ZFH	6
10	3/4	NM Flat Gk, Barium Sulfate filled PTFE, 300 Lbs, RF as per ASME B16.5, Full Face, Thk=1/8in, -,	C7W3AL3K	1
11	5/8	SBlt 2 HHx N, A193 Gr.B7/A194 Gr.2H, -, Xylan PTFE Coated, - 3 in. Length	C6S4K88N	4
12	1/2	SBlt 2 HHx N, A193 Gr.B7/A194 Gr.2H, -, Xylan PTFE Coated, - 2.75 in. Length	C6S4K87U	24
13	1	Plug Flg,SP, Tapered Plug, Non Lubricated, API 599, ASTM A351 Gr.CF8M, 150 Lbs, RF, Ends as per ASME B16.5, -, LO,-, -, Valve Tag: PL-0548	C76KHSRR	2
14	1	Bld Flg, ASME B16.5, ASTM A182 Gr.F304L, 150 Lbs, RF, Annealed,	C7W2U478	1

PIPE SUPPORTS

15	1	PS201-1-S	PS201	4
16	1	PS433-1	PS433	4
17	1	PS709-A-16.52-6	PS709	3
18	1	PS732-3-60-20	PS732	1
19	1	PS212-01	PS212	1
20	1	PS719-H-25.25-6-/	PS719	1

Turner Industries Group, LLC
Received
MARCH 4, 2025
DOCUMENT CONTROL

NOTES:
1. FOR LINE PRESSURES, TEMPERATURES, INSULATION TYPE AND THICKNESS, ETC. REFER TO LATEST REVISION OF LDT.
2. FOR STANDARD PIPE SUPPORT DETAILS SEE PROJECT STANDARD.
3. FIELD SHIM TO SUIT UNLESS OTHERWISE NOTED.
4. FOR PWHT REQUIREMENTS REFER TO LINE CLASS SPECIFICATION.
5. ALL THREADED PIPE LINE SYSTEMS, FIELD SHALL VERIFY DIMENSION PRIOR TO ERECTION.
6. FFW DESIGNATION AT WELDS INDICATES FIELD FIT WELD, WHERE PIPE FABRICATOR IS TO ADD 9 INCH OF PIPE TO THE ISOMETRIC DIMENSION TO ENABLE THE FIELD TO CUT TO FIT AT SITE.
7. REFER TO 202998C-000-W1-1300-0001 FOR FRP AND DUAL-LAM FABRICATION.

TECHNIP ENERGIES

Information contained in this document is the work product of one or more legal entities of Technip Energies N.V. and embodies confidential and proprietary information of the applicable entity and/or its client.use of this information is restricted in accordance with conditions specified by the contract.Technip Energies N.V. and its affiliates disclaim any and all liabilities for any changes or modifications to this document which are made by any person other than the entity that issued the document under the applicable client contract.

THIS DOCUMENT IS UNCONTROLLED WHEN REPRODUCED

REV	DATE	BY	DESCRIPTION	CHKD	MTO	STRESS	APRVD
0	2025-02-28	RVA	ISSUED FOR CONSTRUCTION	SAD	KJK	SMR	GR

SERVICE:	VAPOR/LIQUID:	INSUL TYPE:	INSUL THK:	SHOP:	FIELD:	PAINT CODE:	MODULE:
R2	L	Per LDT	Per LDT	N	Y	Per LDT	-

OXY

OxyChem Redstone Battleground
PROJECT

P&ID: 202998C-001-PID-0021-0331

UNIT#:	EWP AREA:	SPEC:	STRESS CALC #:
6800	6820	EPCL-SS01	-

LINE No. 1"-R2-67147-EPCL-SS01-P

DRAWING NUMBER: 6820-R2-67147-01

REV. 0

27 FEB 2025 03:22
