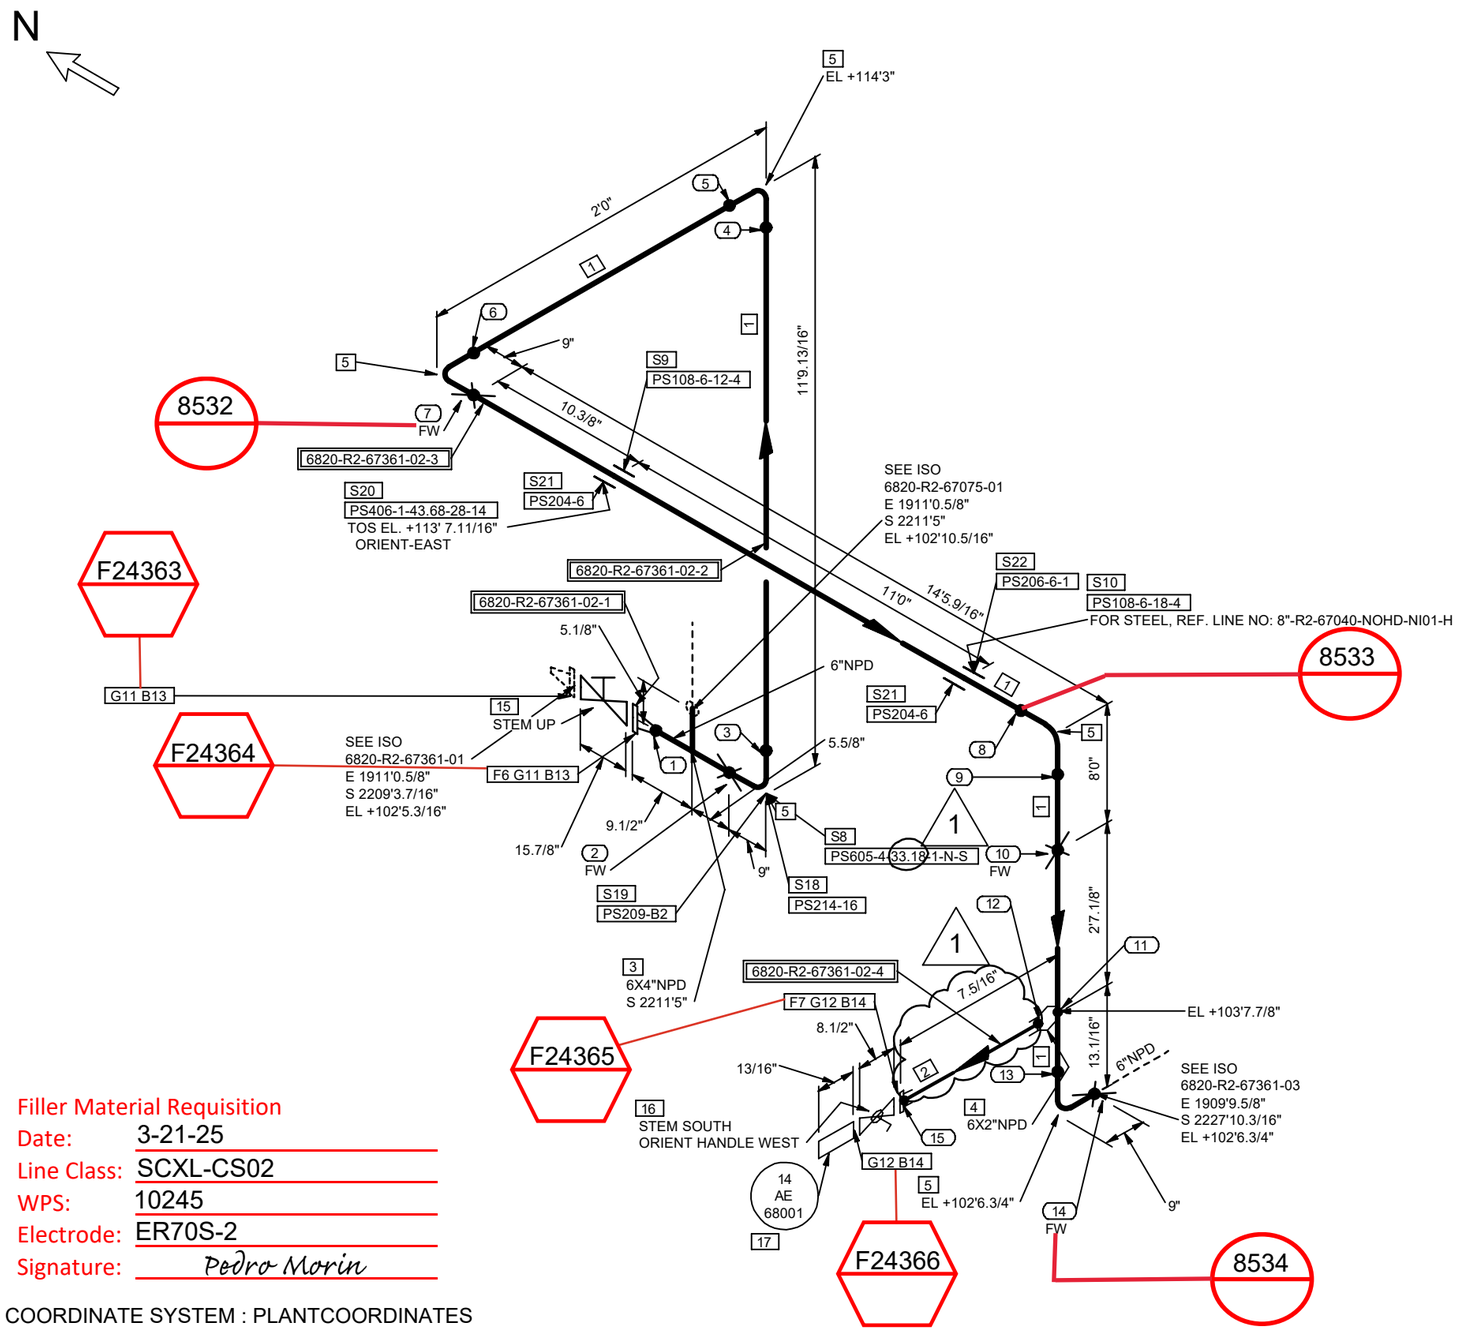

Filler Material Requisition

Date: 3-21-25

Line Class: SCXL-CS02

WPS: 10245

Electrode: ER70S-2

Signature: Pedro Morin

COORDINATE SYSTEM : PLANTCOORDINATES

SHOP MATERIALS

NO	NPD	DESCRIPTION	IDENT	QTY
1	6	Pipes, Seamless, ASME B36.10, ASTM A106 Gr.B, BE, -, S-STD	CPP00336	34.8 '
2	2	Pipes, Seamless, ASME B36.10, ASTM A106 Gr.B, PE, -, -, S-XS	CPPD8UCB	0.2 '
3	6X4	Red Te, Seamless, ASME B16.9, ASTM A234 Gr.WPB, BW Ends, -,-, S-STD	CDB0DGGR	1
4	6X2	Sockolet, ASTM A105N, 3000 Lbs, SW Ends, -, -,	C1HZCKEE	1
5	6	90° Elb LR, Seamless, ASME B16.9, ASTM A234 Gr.WPB, BW Ends, -,-, S-STD	CDB66GNP	5
6	6	WN Flg, ASME B16.5, ASTM A105N, 300 Lbs, RF/BW End, -, S-STD	CFG6WKU7	1
7	2	SW Flg, ASME B16.5, ASTM A105N, 300 Lbs, RF/SW End, -, x S-XS	C1HZCLCV	1

PIPE SUPPORTS

8	6	PS605-4-33.18-1-N-S	PS605	1
9	6	PS108-6-12-4	PS108	1
10	6	PS108-6-18-4	PS108	1

OTHER THAN SHOP MATERIALS

NO	NPD	DESCRIPTION	IDENT	QTY
11	6	NM Flat Gk, Barium Sulfate filled PTFE, 300 Lbs, RF as per ASME B16.5, Full Face, Thk=1/8in, -,	C7CX7CST	2
12	2	NM Flat Gk, Barium Sulfate filled PTFE, 300 Lbs, RF as per ASME B16.5, Full Face, Thk=1/8in, -,	C7CX7CSL	2
13	3/4	SBlt 2 HHx N, A193 Gr.B7/A194 Gr.2H, -, Xylan PTFE Coated, - 5 in. Length	C6S4K8BF	24
14	5/8	SBlt 2 HHx N, A193 Gr.B7/A194 Gr.2H, -, Xylan PTFE Coated, - 3.5 in. Length	C6S4K88R	16
15	6	Gat Flg, -, API 600, ASTM A216 Gr.WCB,300 Lbs, RF, Ends as per ASME B16.5, HO,-, Valve Tag: GA-1192	C99ZZ9EJ	1
16	2	Bal Flg,FB,SP, API 608, ASTM A216 Gr.WCB,300 Lbs, RF, Ends as per ASME B16.5,-, LO,-, Valve Tag: BA-1097	C9YR0U5Z	1

INSTRUMENTS

17	2	14-AE-68001	14-AE-68001	1

PIPE SUPPORTS

18	6	PS214-16	PS214	1
19	6	PS209-B2	PS209	1
20	6	PS406-1-43.68-28-14	PS406	1
21	6	PS204-6	PS204	2
22	6	PS206-6-1	PS206	1

PIECE MARKS

6820-R2-67361-02-1 6820-R2-67361-02-2 6820-R2-67361-02-3
6820-R2-67361-02-4

Turner Industries Group, LLC
Received
MARCH 20, 2025
DOCUMENT CONTROL

NOTES:

1. FOR LINE PRESSURES, TEMPERATURES, INSULATION TYPE AND THICKNESS, ETC. REFER TO LATEST REVISION OF LDT.
2. FOR STANDARD PIPE SUPPORT DETAILS SEE PROJECT STANDARD.
3. FIELD SHIM TO SUIT UNLESS OTHERWISE NOTED.
4. FOR PWHT REQUIREMENTS REFER TO LINE CLASS SPECIFICATION.
5. ALL THREADED PIPE LINE SYSTEMS, FIELD SHALL VERIFY DIMENSION PRIOR TO ERECTION.
6. FFW DESIGNATION AT WELDS INDICATES FIELD FIT WELD, WHERE PIPE FABRICATOR IS TO ADD 9 INCH OF PIPE TO THE ISOMETRIC DIMENSION TO ENABLE THE FIELD TO CUT TO FIT AT SITE.
7. REFER TO 202998C-000-W1-1300-0001 FOR FRP AND DUAL-LAM FABRICATION.

TECHNIP ENERGIES

Information contained in this document is the work product of one or more legal entities of Technip Energies N.V. and embodies confidential and proprietary information of the applicable entity and/or its client.use of this information is restricted in accordance with conditions specified by the contract.Technip Energies N.V. and its affiliates disclaim any and all liabilities for any changes or modifications to this document which are made by any person other than the entity that issued the document under the applicable client contract.

THIS DOCUMENT IS UNCONTROLLED WHEN REPRODUCED

REV	DATE	BY	DESCRIPTION	CHKD	MTO	STRESS	APRVD
1	2025-03-14	RVA	ISSUED FOR CONSTRUCTION	SAD	KJK	SMR	GR
0	2025-01-31	RVA	ISSUED FOR CONSTRUCTION	SAD	KJK	SMR	GR

SERVICE:	VAPOR/LIQUID:	INSUL TYPE:	INSUL THK:	SHOP:	FIELD:	PAINT CODE:	MODULE:
R2	L	Per LDT	Per LDT	Y	Y	Per LDT	-

OXY

OxyChem Redstone Battleground
PROJECT

P&ID: 202998C-001-PID-0021-0325

UNIT#:	EWP AREA:	SPEC:	STRESS CALC #:
6800	6820	SCXL-CS02	CN-0394

LINE No. 6"-R2-67361-SCXL-CS02-H

DRAWING NUMBER 6820-R2-67361-02

REV. 1

15 MAR 2025 03:47
