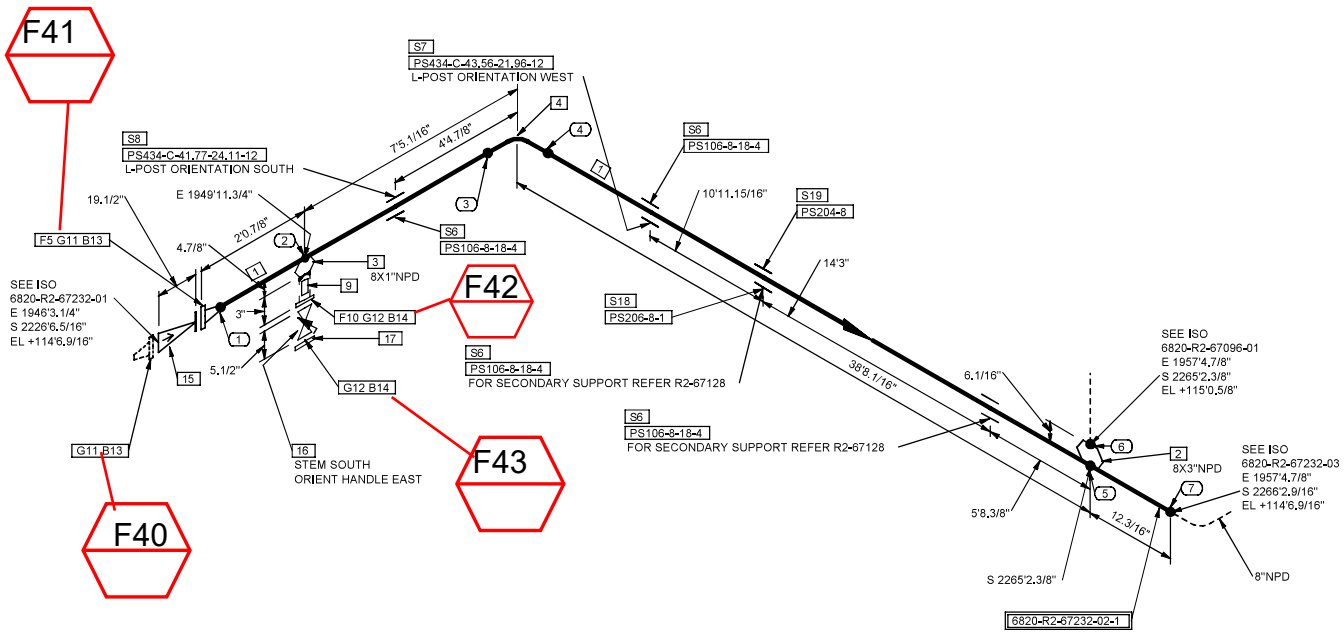

Filler Material Requisition

Date: 6-5-24

Line Class: EPCL-SS01

WPS: N/A

Electrode: NO FIELD WELDS

Signature: Glenn Sumrall

COORDINATE SYSTEM : PLANTCOORDINATES

SHOP MATERIALS

NO	NPD	DESCRIPTION	IDENT	QTY
1	8	Pipes, Seamless, ASME B36.19/B36.10, ASTM A312 Gr.TP304L, BE, -, -, S-10S	C7FCT25	46.9 '
2	8X3	Weldolet, MSS SP-97, ASTM A182 Gr.F304L, BW Ends, Annealed, S-10S	C7BP7VPP	1
3	8X1	Threadolet, ASTM A182 Gr.F304L, 3000 Lbs, NPTF Ends, -, Annealed,	C7BP7RN7	1
4	8	90° Elb LR, Seamless, ASME B16.9, ASTM A403 Gr.WP304L, BW Ends, -, Annealed, S-10S	C6SEUJRF	1
5	8	WN Flg, ASME B16.5, ASTM A182 Gr.F304L, 150 Lbs, RF/BW End, Annealed, S-10S	C7W2U6T4	1
		PIPE SUPPORTS		
6	8	PS106-8-18-4	PS106	4
7	8	PS434-C-43.56-21.96-12	PS434	1
8	8	PS434-C-41.77-24.11-12	PS434	1

OTHER THAN SHOP MATERIALS

NO	NPD	DESCRIPTION	IDENT	QTY
9	1	Nipple, ASTM A312 Gr.TP304L, NPTM Ends, L = 3in, -, S-80S	CEZMKL0	1
10	1	THD Flg, ASME B16.5, ASTM A182 Gr.F304L, 150 Lbs, RF/NPTF End, Annealed,	C7W2U48L	1
11	8	NM Flat Gk, Barium Sulfate filled PTFE, 150 Lbs, RF as per ASME B16.5, Full Face, Thk=1/8in, -,	C7CT1ZG2	2
12	1	NM Flat Gk, Barium Sulfate filled PTFE, 150 Lbs, RF as per ASME B16.5, Full Face, Thk=1/8in, -,	C7CT1ZFH	2
13	3/4	SBlt 2 HHx N, A193 Gr.B7/A194 Gr.2H, -, Xylan PTFE Coated, -, 4.5 in, Length	C6S4K8BD	16
14	1/2	SBlt 2 HHx N, A193 Gr.B7/A194 Gr.2H, -, Xylan PTFE Coated, -, 2.75 in, Length	C6S4K87U	8
15	8	SwgChk Flg, ASME B16.34, ASTM A351 Gr.CF8M,150 Lbs, RF, Ends as per ASME B16.5,-, Valve Tag: CH-0276	C76KHSRG	1
16	1	Plug Flg,SP, Tapered Plug, Non Lubricated, API 599, ASTM A351 Gr.CF8M, 150 Lbs, RF, Ends as per ASME B16.5, -, LO,-, -, Valve Tag: PL-0548	C76KHSRR	1
17	1	Bld Flg, ASME B16.5, ASTM A182 Gr.F304L, 150 Lbs, RF, Annealed,	C7W2U478	1
		PIPE SUPPORTS		
18	8	PS206-8-1	PS206	1
19	8	PS204-8	PS204	1

PIECE MARKS

6820-R2-67232-02-1

Turner Industries Group, LLC
Received
June 4,2024
DOCUMENT CONTROL

NOTES:
1. FOR LINE PRESSURES, TEMPERATURES, INSULATION TYPE AND THICKNESS, ETC. REFER TO LATEST REVISION OF LDT.
2. FOR STANDARD PIPE SUPPORT DETAILS SEE PROJECT STANDARD.
3. FIELD SHIM TO SUIT UNLESS OTHERWISE NOTED.
4. FOR PWHT REQUIREMENTS REFER TO LINE CLASS SPECIFICATION.
5. ALL THREADED PIPE LINE SYSTEMS, FIELD SHALL VERIFY DIMENSION PRIOR TO ERECTION.
6. FFW DESIGNATION AT WELDS INDICATES FIELD FIT WELD, WHERE PIPE FABRICATOR IS TO ADD 9 INCH OF PIPE TO THE ISOMETRIC DIMENSION TO ENABLE THE FIELD TO CUT TO FIT AT SITE.

T.EN TECHNIP ENERGIES

information contained in this document is the work product of one or more legal entities of Technip Energies N.V. and embodies confidential and proprietary information of the applicable entity and/or its client,use of this information is restricted in accordance with conditions specified by the contract.Technip Energies N.V. and its affiliates disclaim any and all liabilities for any changes or modifications to this document which are made by any person other than the entity that issued the document under the applicable client contract.
THIS DOCUMENT IS UNCONTROLLED WHEN REPRODUCED

REV	DATE	BY	DESCRIPTION	CHKD	MTO	STRESS	APRVD
0	17/05/2024	RVA	ISSUED FOR CONSTRUCTION	SAD	KJK	BRD	GR

SERVICE:	VAPOR/LIQUID:	INSUL TYPE:	INSUL THK:	SHOP:	FIELD:	PAINT CODE:	MODULE:
R2	L	Per LDT	Per LDT	Y	N	Per LDT	-

OXY

OxyChem Redstone Battleground PROJECT

P&ID: 202998C-001-PID-0021-0331

UNIT#	EVP AREA	SPEC:	STRESS CALC #
6800	6820	EPCL-SS01	NC

LINE No. 8"-R2-67232-EPCL-SS01-H

DRAWING NUMBER: 6820-R2-67232-02

REV.: 0

17 MAY 2024 09:04
